




माप्य दुधकोशी गाउँपालिका
गाउँ कार्यपालिकाको कार्यालय

खास्ताप, मोलुखुम्बु
प्रदेश नं. १ नेपाल

नं. : २०७९/०८०

तः ३३६



मिति : २०७९/०५/३१

श्री आर्थिक मामिला तथा योजना मन्त्रालय,
प्रदेश नं. १ विराटनगर, ।


विषय : प्रगति विवरण पठाईएको सम्बन्धमा ।

प्रस्तुत विषयमा यस माप्य दुधकोशी गाउँपालिकामा आ.व. २०७८/७९ मा सञ्चालित प्रदेश समपुरक अनुदानका आयोजना तथा कार्यक्रमको प्रगति विवरण यसै पत्रसाथ संलग्न गरि पठाईएको व्यहोरा अनुरोध छ ।

गजेन्द्र भट्टराई
नि. प्रमुख प्रशासकीय अधिकृत



माध्यम दुधकोशी गाउँपालिका
गाउँ कार्यपालिकाको कार्यालय



म. : २०७९/०८०

न. : ३३५

मिति : २०७९/०५/३१


श्री प्रदेश लेखा नियन्त्रक कार्यालय,
प्रदेश नं. १, विराटनगर, मोरङ।

विषय : प्रगति विवरण पठाईएको सम्बन्धमा।

प्रस्तुत विषयमा यस माध्यम दुधकोशी गाउँपालिकामा आ.व. २०७८/७९ सञ्चालित प्रदेश समपुरक अनुदानका आयोजना तथा कार्यक्रमको प्रगति विवरण यसै पत्रसाथ संलग्न गरि पठाईएको व्यहोरा अनुरोध छ।

गजेन्द्र भट्टराई
नि. प्रमुख प्रशासकीय अधिकृत

प्रगति विवरण संकलन फारम



१	जिल्ला	सोलुखुम्बु	
२	स्थानीय तहको नाम	माथ्य दुधकोशी गाउँपालिका	
३	स्वीकृत आयोजना कार्यक्रमको नाम	थानेखोला खानेपानी आयोजना	
४	स्वीकृत रकम	१०३००४४०	
५	कार्यक्रम कार्यान्वयन विधि	ठेकेदार मार्फत	
६	आयोजना कार्यक्रम कार्यान्वयनका लागि सम्झौता गरिएको संस्थाको नाम	चण्डेश्वरी कन्स्ट्रक्सन	
७	आयोजना कार्यक्रम कार्यान्वयनका लागि सम्बन्धित संस्थासँग गरिएको सम्झौता मिति	२०७९/०२/२४	
८	सम्झौता रकम	१०	
९	भुक्तानी रकम	६४२२३५५	
१०	आयोजना कार्यक्रम कार्यान्वयनका लागि स्वीकृत बजेट वचत हुन गई पुन खरिद सम्झौता भएको/नभएको	भएको	✓ नभएको
११	आयोजना कार्यक्रम कार्यान्वयनका लागिपुन सम्झौता भएको हकमा मात्र		
१२	आयोजना कार्यक्रम कार्यान्वयनका लागि सम्झौता गरिएको संस्थाको नाम	चण्डेश्वरी कन्स्ट्रक्सन	
१३	आयोजना कार्यक्रम कार्यान्वयनका लागि सम्बन्धित संस्थासँग गरिएको सम्झौता मिति	२०७९/०२/२४	
१४	सम्झौता मिति	१०३००००००	
१५	भुक्तानी मिति	६४२२३५५	
१६	कुल भुक्तानी रकम (क्र.स. ८ र १४ को योगफल)		
१७	संलग्न कागजातहरु		
१८	आयोजना कार्यक्रम कार्यान्वयनका लागि सम्बन्धित संस्थासँग गरिएको खरिद सम्झौताको प्रमाणित प्रतिलिपि		
१९	भुक्तानीसँग सम्बन्धित गोश्वरा भौचरको प्रमाणीत प्रतिलिपि		
२०	आयोजनासँग सम्बन्धित प्रष्ट बुझिने फोटो		
२१	सुझावहरु		
२२	नीतिगत सुझावहरु (प्रदेश समपुरक अनुदान सम्बन्धि कार्यविधिमा आधारित भएर पदान गरिने सुझावहरु)		
२३	अन्य सुझावहरु (स्वीकृत कार्यक्रमको कार्यान्वयनसँग सम्बन्धित सुझावहरु)		



माध्यमिक शिक्षा गाउँपालिका
गाउँ कार्यपालिकाको कार्यालय, सोलुखुम्बु



म.ले.प.फा.नं. २०३

आ.व. : २०७८/७९

कोष : खर्च खाता

बजेट उपशीर्षक : प्रदेश सरकारबाट हस्तान्तरित कार्यक्रम - ८०१०१५०२५०२

विद्युतीय कारोवार नं. : ४१३४८५२८२५३५३९९०६

गो. भौ. नं. : ८

पूँजीगत

मिति : २०७९/०३/२५

सि.नं.	संकेत / उप-शीर्षक नम्बर	क्रियाकलाप/ कार्यक्रम संकेत नं	कारोवारको व्यहोरा	खा.पा.नं.	स्रोत			डेबिट	क्रेडिट
					स्रोत व्यहोने संस्था	प्रकार	भुक्तानी विधि		
१	३११५१	१	डे. बजेट खर्च [प्रदेश सरकार बाट प्राप्त समपुरक अनुदान]		प्रदेश नम्बर १	अनुदान	नगद	६४,२२,३५५	०
२	३११५१	१	क्रे. चण्डेश्वरी कन्स्ट्रक्सनपेशकी फर्छौट, [प्रदेश सरकार बाट प्राप्त समपुरक अनुदान]		प्रदेश नम्बर १	अनुदान	नगद	०	२०,००,०००
३			क्रे. बैंक, कृषि विकास बैंक लिमिटेड, ११२५६०१५०६५०८०३९					०	४४,२२,३५५
जम्मा								६४,२२,३५५	६४,२२,३५५

जम्मा रकम अक्षरमा : रुपैयाँ चौसठ्ठी लाख बाइस हजार तिन सय पचपन्न मात्र ।

कारोबारको व्यहोरा

थानेखार्ल खानेपालि लाइ प्रथम रनिङ विल भुक्तानि दिदाको लेखा

कारोबारको पुष्ट्याई विवरण फारम नं. मा भरी संलग्न गरिएको छ ।

संलग्न कागजात संख्या :

भुक्तानी प्रयोजन का लागि

भुक्तानी पाउनेको नाम	भ्याट/प्यान	बैंक/खाता नं.	Voucher/Cheque/eft No	भुक्तानी रकम	अक्षरेपी रु	दस्तखत
१ चण्डेश्वरी कन्स्ट्रक्सन	६०५५७६८५६		१९५५०३८३	४४,२२,३५५	रुपैयाँ चवालिस् लाख बाइस हजार तिन सय पचपन्न मात्र ।	

तयार गर्ने : खगेन्द्र भट्टराई

पद : लेखापाल

मिति : २०७९/०३/२५

प्रतिष्ठि गर्ने : ८०१११५०२

पेश गर्ने : खगेन्द्र भट्टराई

पद : लेखापाल

मिति : २०७९/०३/२५

सदर गर्ने : जितेन्द्र कुमार पादव

पद : अधिकृत आठौं

मिति : २०७९/०३/२५



चण्डेश्वरी कन्स्ट्रक्शन Chandeshori Construction

ई.प्र.न. ५/२०७७/७८
प्रा.प्र.प.नं. २२३५/०७७/०७८
स्थाई ले.न. ६०५५७६८५६

प.सं. ०६८/६९
च.नं. ५०

लिखुपिके गा.पा.-२, सोलुखुम्बु
Likhupike R.M.-Solukhumbu

मिति २०६९/०३/१६

श्री कामोत्तम फ्याल्ज ड्या
भाज्ज इङ्गेकोशी गाउँपालिका को कामोत्तम खोलखुम्बु ।

बिषय: रनिङ.विल उठाई भुक्तानी गरि जाउँ ।

प्रस्तुत विषयमा त्रु कामोत्तम र चण्डेश्वरी कन्स्ट्रक्शन बिच
२०६८/११/२६ का दिन विधिगत रूपमा सम्झौता भएको भेजना
हेक्का नं. MDRM-०२-२०७८/०७९. Construction of Thane-
khola Water Supply project निमाबधीन कार्रवाया भै रहेकोले
आवश्यक प्राविशमा पुग्दा रनिङ.विल आपाई उठाई भुक्तानी गरि दिनु
हुन भै निवेदन गर्दछु ।

श्री प्रादेश्वर २०७८
रनिङ. विल उठाई दिनु हुन
बोधार्थ



निवेदन

रेल बहादुर बान्तो
सल्लेरी -५ सोलुखुम्बु
९८४९०४२३०६



चण्डेश्वरी कन्स्ट्रक्सन Chandeshori Construction

प.सं. ०८८/८९
च.नं. ११

लिखुपिके गा.पा.-२, सोलुखुम्बु
Likhupike R.M.-Solukhumbu

मिति: २०७५/०२/२३

श्री कार्यालय प्रमुख ज्यू
माप्य दुधकोशी गाउँपालिकाको कार्यालय
खास्ताप, सोलुखुम्बु

बिषय: म्याद थप गरि पाऊँ ।

प्रस्तुत विषयमा यस माप्यदुधकोशी गाउँपालिका र चण्डेश्वरी कन्स्ट्रक्सन विच मिति २०७८/११/२७ का दिन विधिगत रुपमा सम्झौता भई निर्माणाधिन अवस्थामा रहेको ठेक्का नं. MDRM-07-2078/079 THANE KHOLA WATER SUPPLY PROJECT UNDER INVITATION योजनाको विविध कारणहरु स्थानिय तहको निर्वाचन, डिजेल, पेट्रोल तगायत विभिन्न निर्माण सामाग्रीको मूल्य वृद्धि र छिटो वर्षा अधिक भएको कारणले समयमा नै कार्य सम्पन्न गर्न गाह्रो परेको हुदाँ आजका मितिले १ वर्ष सम्म कार्य सम्पन्न गर्ने गरि म्याद थप गरि दिनु हुन यो निवेदन गर्दछु ।

श्री कृष्ण शर्मा
दाता श्रीमान

निवेदक

रेख बहादुर बस्नेत

लिखुपिके गा.पा.-२, सोलुखुम्बु

९८४९०४२६०७





माप्य दुधकोशी गाउँपालिका
गाउँ कार्यपालिकाको कार्यालय
खास्ताप, सोलुखुम्बु
१ नं. प्रदेश नेपाल

पत्र संख्या - ०७८/०७९

चलानी नं.- १२७४



मिति २०७९/०३/०१

श्री चण्डेश्वरी कन्स्ट्रक्सन प्रा.लि.

लिखुपिके २, सोलुखुम्बु ।

विषय : म्याद थप गरिएको सम्बन्धमा ।

श्रीमान्,

प्रस्तुत विषयमा त्यस कार्यालयको मिति २०७९/०२/२३ गतेको प्राप्त पत्रानुसार यस कार्यालय र त्यस फर्म विच मिति २०७८/११/२७ को सम्झौता अनुसार ठेक्का नं MDRM-07-2078/079 को Construction of Thane khola water Supply Project को हाल कार्य अघि बढिरहेको र अत्याधिक वर्षा र २०७९को स्थानिय चुनावले गर्दा कार्य केहि ढिला हुन गएकोले यस पत्रको समाप्त सम्झौता मितिले बाँकी कार्य सम्पन्न गर्न मिति २०७९/०६/२४ गते सम्मको लागि ३ महिना म्याद थप गरिएको व्यहोरा अनुरोध छ ।

७०५५५

७०५५५

जितेन्द्र कुमार यादव

नि प्रमुख प्रशासकीय अधिकृत



माप्य दुधकोशी गाउँपालिका
गाउँ कार्यपालिकाको कार्यालय

खास्ताप, सोलुखुम्बु
१ नं. प्रदेश, नेपाल

पत्र संख्या:-०७८/०७९

च.नं.:- १२१९



मिति: २०७९/०३/१३

M/S Chandeshwori Construction,
Likhupike 2, Solukhumbu

विषय: बैंक जमातन नविकरण गरी पेश गर्ने सम्बन्धमा।

प्रस्तुत विषयमा यस कार्यालयको खरिद सम्झौता नं. MDRM-07-2078/079 सोलुखुम्बु जिल्ला Construction of Thane Khola Water Supply Project निर्माण कार्यका लागि पेश गरिएको तपशिल बमोजिमको बैंक ग्यारेण्टी म्याद थप प्रयोजनको लागि नियमानुसार नविकरण गरिदिनु हुन अनुरोध छ।

तपसिल

सि.न.	जमानी नं.	जमानी रकम	मान्य अवधि	जमातन थप गर्नु अवधि	निर्माण व्यवसायी	कैफियत
१.	MD2206938109	520000	August 2, 2023	November 2 2023	M/S Chandeshwori Construction Likhupike 2, Solukhumbu	

जितेन्द्र कुमार शर्मा
नि.प्रमुख प्रशासकीय अधिकृत

बोधार्थ:

श्री कृषि विकास बैंक लि, शाखा कार्यालय सोलुखुम्बु: नियमानुसार नविकरण गरिदिनु हुन।

“व्यवसायिक र सृजनशील प्रशासन: विकास, समृद्धि र सुशासन”



Classmate. रेव कदाहु बान्जिहे
सबान्जिहे - ५ होलुबुलु
३८४३०४२३०४

कर विज्ञापन
चण्डेश्वरी कन्स्ट्रक्सन

लिखुपिके गा.पा-२, सोलुखुम्बु

विज्ञापन नं. : 05

विक्रेताको भ्याट नं.

६ ० ५ ५ ७ ६ ८ ५ ६

क्रेताको नाम : माप्य इधकोशी गाउँपालिका

ठेगाना : खोस्वा, सोलुखुम्बु

कारोबार मिति : २०७९-०३-१७

क्रेताको भु.अ.कर दर्ता नं.

विज्ञापन जारी मिति :

भुक्तानीको क्रिसिम : नगद/उधारो/चेक

सि.नं.	विवरण	परिमाण	प्रति इकाई मूल्य		जम्मा मूल्य	
			रु.	पै.	रु.	पै.
१)	Construction of Thane Khola Water Supply Project	१	—		५६,८३,५००/-	
भारेफी र चौखोती लारव बाइस हजार तीन सय पच्चीस रुपैया मात्र ।			जम्मा रकम		५६,८३,५००/-	
			प्रतिशत छुट			
			कर लाग्ने मूल्य		५६,८३,५००/-	
			१३ % भ्याट		७,३८,८५२/-	
			जम्मा		६४,२२,३५२/-	

क्रेताको सही


विक्रेताको सही



माप्य दुधकोशी गाउँपालिका
गाउँ कार्यपालिकाको कार्यालय

खास्ताप, सोलुखुम्बु

१ नं. प्रदेश, नेपाल

माप्य दुधकोशी गाउँपालिकाको कार्यालय
खास्ताप, सोलुखुम्बु,
१ नं. प्रदेश, नेपाल

पत्र संख्या :- ०७८/०७९

च.नं.:- १३४४

मिति : २०७९/०३/१९

प्रतिवेदन

यस माप्य दुधकोशी गाउँपालिकाद्वारा जारी गरिएको **Construction of Thane Khola Water Supply Project** ठेक्का नं **MDRM-01-2079/079** को मिति २०७८/११/२७ मा चण्डेश्वरी कन्स्ट्रक्सन प्रा. लि.सँग सम्झौता भई निर्माणाधीन रहेको र सो ठेक्काको हाल सम्म भएको कार्यको चेकजाच गर्दा प्राविधिक स्टामेट र BOQ अनुसार रहेका व्यहोरा अनुरोध छ ।

ई. जोनाथन राई

इन्जिनियर

माप्य दुधकोशी गाउँपालिका

जोनाथन खालिङ राई
इन्जिनियर
माप्य दुधकोशी गा.पा.

Mapya Dudhkoshi Rural Municipality

Thane Khola , Waku , Solukhumbu

Name Of Project: Construction of Thane Khola Water Supply Project

1st Running Bill (Abstract of Cost)

Contract No. MDRM-07-2078/079

S.N.	Description	Unit	Quantity	Rate	Amount (NRs.)	Amount In Words	Remarks
1	Site Clearance, Thick Grasscutting, root Excavations, Site Preparation with mud Cutting with 25m Lead	Sqm	300	500	150000	One Lakhs Fifty Thosund Rupees	
2	Earthwork Excavation for Foundation of Different Structures in Ordinary Soil	Cum	30	1000	30000	Thirty Thousand Ruppes	
7	Dry Stone Soling Works	Cum	4	5000	20000	Twenty Thousand Rupees	
9	1:2:4 PCC Works in Foundation and floor including material collection and transportation upto 30m	Cum	4	20000	80000	Eigthy Thousand Rupees	
13	Rubble Stone Masorny Works in 1:4 Cement sand mortar and including 10m transportation	Cum	10	10000	100000	One Lakhs Rupess	
28	600 m circular metal manhole cover for tank as per standard details	No.s	13	2000	26000	Twenty Six Thousand Rupees	
32	Pipe And Fitting For structures	LS	1	30000	30000	Thirty Thousand Rupees	
33	HDPE Pipe Cost 75 mm 10kg	RM	2900	500	1450000	Fourteen Lakhs Fifty Thousand Rupees	
34	HDPE Pipe Cost 75 mm 16 kg	RM	1200	500	600000	Six Lakhs Rupees	
35	HDPE Pipe Cost 25 mm 12.5 kg	RM	50	150	7500	Seven Thousand Five Hundred Rupees	
36	HDPE Pipe Cost 63 mm 10 kg	RM	1500	250	375000	Three lakhs seventy five thousand Rupees	
	HDPE Pipe Cost 32 mm 10 kg	RM	400	100	40000	Fourty thousand rupees	
38	HDPE Pipe Cost 32 mm 16 kg	RM	300	250	75000	Seventy Thousand Rupees	
45	GI Pipe 65mm Medium Class Cost	RM	1800	1500	2700000	Twenty Seven Lakhs Rupees	
	Total = (NRs.)				5,683,500.00	Fifty Six Lakhs Eighty Three Thousand and Five Hundred	
	13% VAT = (NRs.)				738,855.00	Seven Lakhs Thirty Eight Thousand Eight Hundred and Fifty Five	
	Grand Total = (NRs.)				6,422,355.00	Sixty Four Lakhs Twenty Two Thousand Three Hundred And Fifty Five	

11/11/2018

ThaneKhola , Waku , Solukhumbu

1st Running Bill (Detail Quantity Measurement Sheet)

Contract No. MDRM-07-2078/079

S.N.	Description	No.	Radius	Length	Breadth	Height	Unit	Quantity	Remarks
1	Site Clearance, Thick Grasscutting, root Excavations, Site Preparation with mud Cutting with 25m Lead			30	23	0.43	m2	300	
	Total of 1						m2	300	
2	Earthwork Excavation for Foundation of Different Structures in Ordinary Soil								
2.1	Intake With CC(Collection Chamber)								
	Wing Wall	1		4.60	0.45	1.70		3.519	
	Collection Chamber	1		2.30	1.80	1.00		4.14	
	Catchement portion	1		2.50	0.7	1.00		1.75	
	Projection of concreton inside catchment portion.	1		2.10	0.4	0.20		0.168	
	Pipe trench for washout	1		10.00	0.45	0.90		4.05	
	Drainage ditch (15m long)	1		15.00	0.2	0.30		0.9	
	Sub Total						m3	14.527	
	Sedimentation Tank								
	Valve Chamber	1		1.70	1.50	1.30		3.32	
	Sedimentation tank	1	1.31			1.00		5.31	
	(Q = - x r ² x h, r = d/2+0.05+0.75, d = 3.5 m)								
	Washout pipe trench	1		10.00	0.60	0.90		5.40	
	Sub Total						m3	14.03	
2.3	Tap Stand								
	Rear Wall	2		0.6	0.35	0.4		0.168	
	Standpost Walls	1		1.9	0.35	0.4		0.266	
	Small Chamber	1		0.35	0.35	0.35		0.042875	
	Drain	1		5	0.45	0.6		1.35	
	Sub Total						m3	1.83	
	Total Of 2						m3	30.000	
7	Dry Stone Soling Works								
7.1	Boulder soling For Intake	1		1.05	1.8	0.15	m3	0.2835	
	Dry stone soling work for Distribution Chamber	2		3.60	1.85	0.15	m3	2	
7.3	Dry Stone Soling With Sand	5		1.9	1.7	0.1	m3	1.62	
	Small Chamber	5		0.35	0.35	0.1	m3	0.06	
	Sub Total						m3	1.68	
	Total 7						m3	4.00	
9	1:2:4 PCC Works in Foundation and floor including material collection and transportation upto 30m	1		1.5	1.5	1.78	m3	4	
13	Rubble Stone Masorny Works in 1:4 Cement sand mortar and including 10m transportation								

A handwritten signature in black ink, appearing to be "S. J.", written over a horizontal line.

Spring

13.1	Stone masonry 1:4 cement mortar								
	Wing Wall	1		4.60	0.45	1.35		2.79	
	Deduction for dry wall	1		0.70	0.45	0.50		-0.16	
	Collection Chamber							0.00	
	Long Wall	2		1.15	0.45	0.60		0.62	
	Long Wall	2		1.05	0.35	0.80		0.59	
	Short Wall	1		0.70	0.45	0.70		0.22	
	Short Wall	1		0.90	0.35	0.80		0.25	
	Deduction for embedment block	1		0.50	0.45	0.30		-0.07	
		1		0.50	0.35	0.30		-0.05	
						Sub Total	m3	1.56	
13.2	Stone masonry work in 1:4 cement mortar For Distribution Chamber (DC)	2							
		1		1.65	0.45	1.10			
		1		1.65	0.45	1.30			
		2		1.65	0.45	1.10			
		2		0.70	0.45	1.30			
		1		0.75	0.45	0.65			
						Sub Total	m3	8.92	
	Total of 13						m3	10	
	600 m circular metal manhole cover for tank as per standard details						no.s	13	
32	Pipe And Fitting For structures						LS	1	
33	HDPE Pipe Cost 75 mm 10kg						2900	RM	
34	HDPE Pipe Cost 75 mm 16 kg						1200	RM	
35	HDPE Pipe Cost 25 mm 12.5 kg						50	RM	
36	HDPE Pipe Cost 63 mm 10 kg						1500	RM	
37	HDPE Pipe Cost 32 mm 10 kg						400	RM	
38	HDPE Pipe Cost 32 mm 16 kg						300	RM	
45	GI Pipe 65mm Medium Class Cost						1800	RM	




Prepared By:



अ. सव. इंजीनियर
सूर्य रेग्मी मगर


Checked By:

जोनाथन खोचि राई
इन्जिनियर
माध्य दधकोशी गा.पा

Approved By:

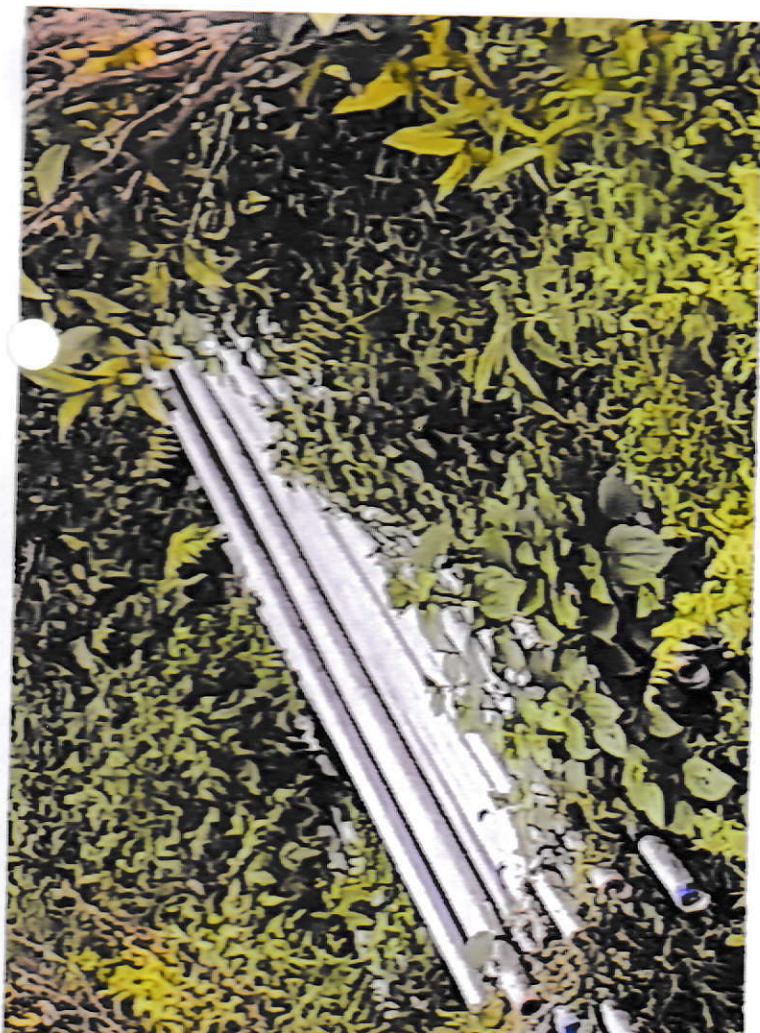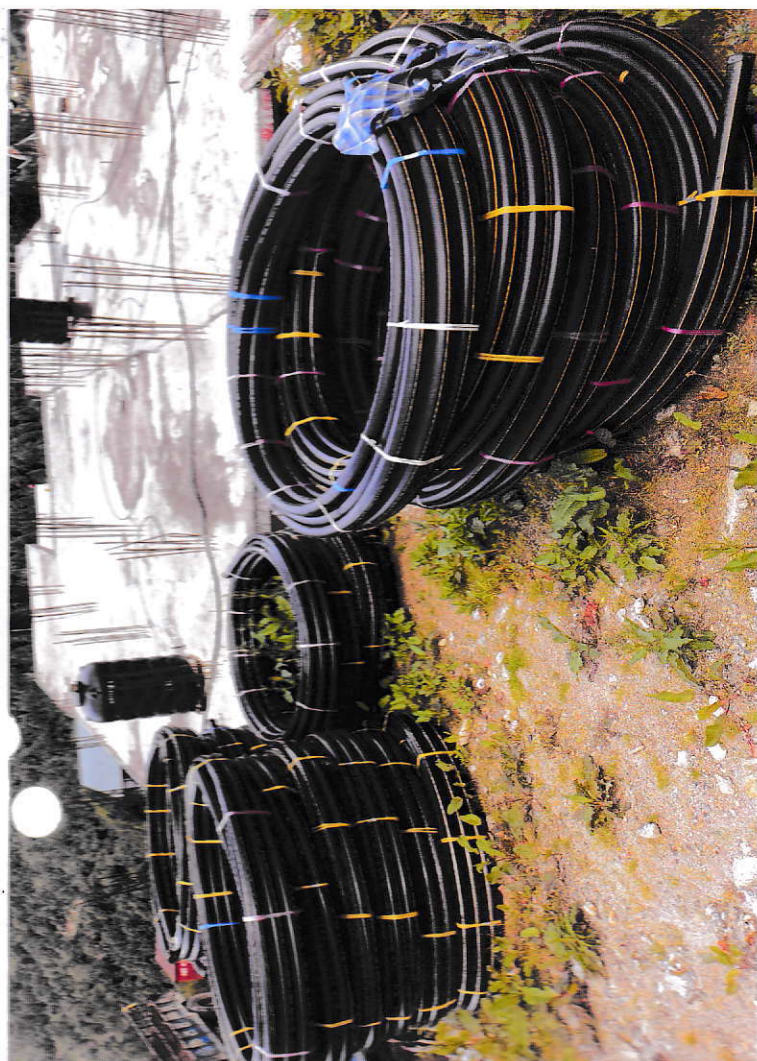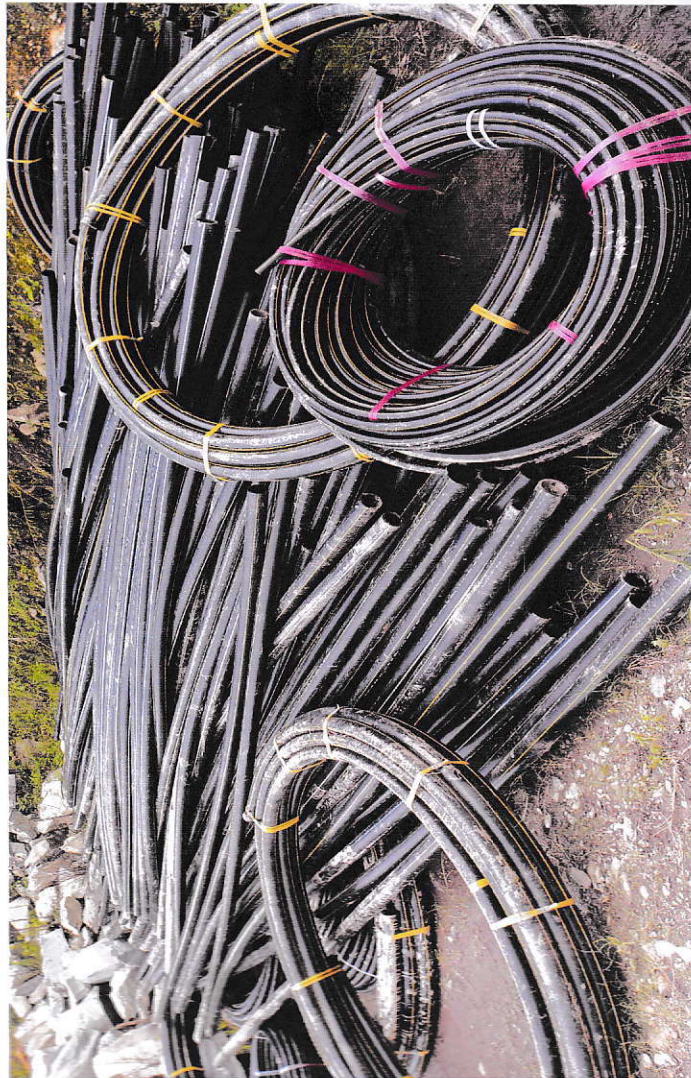

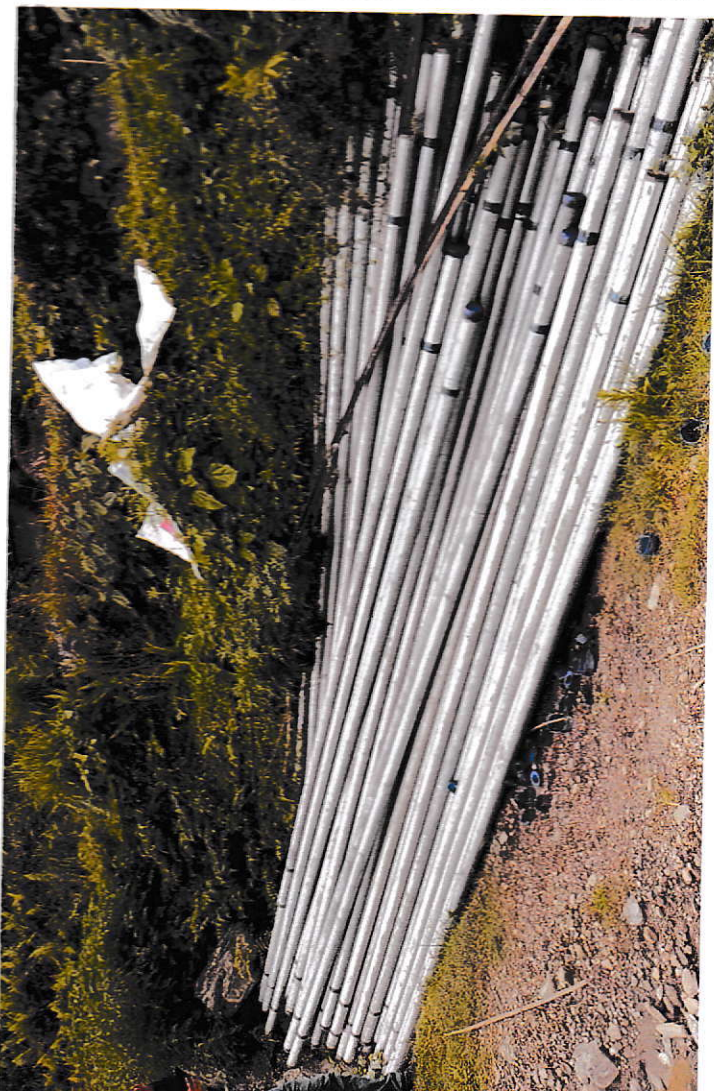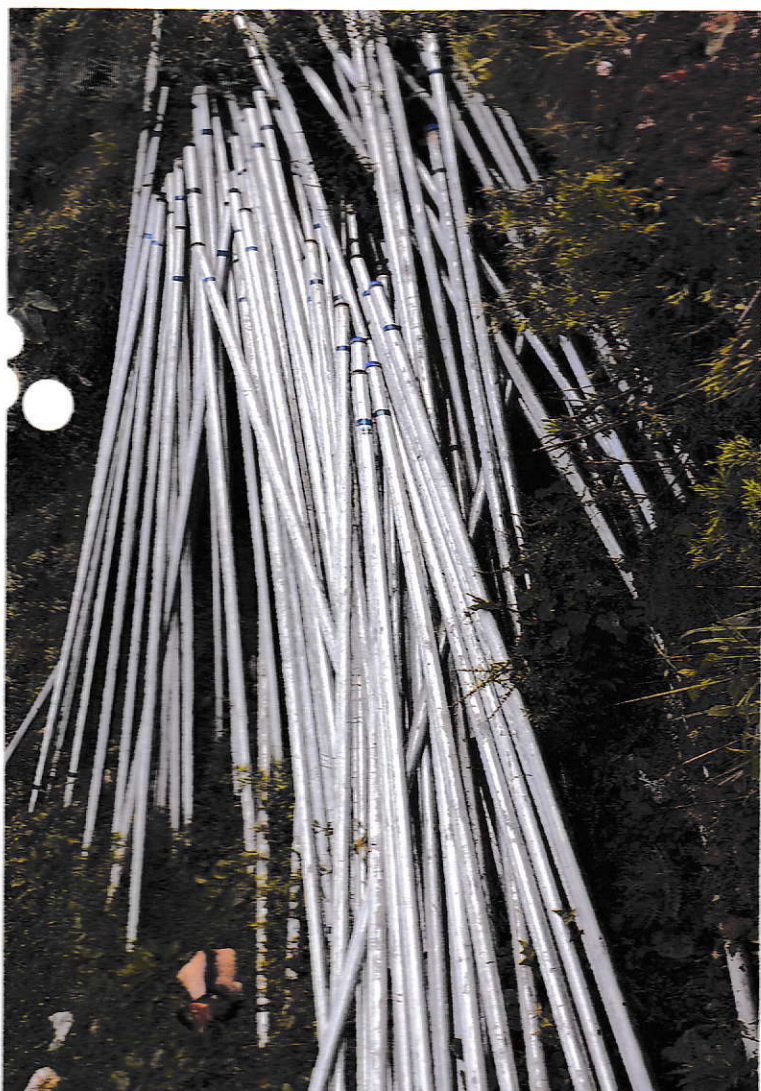

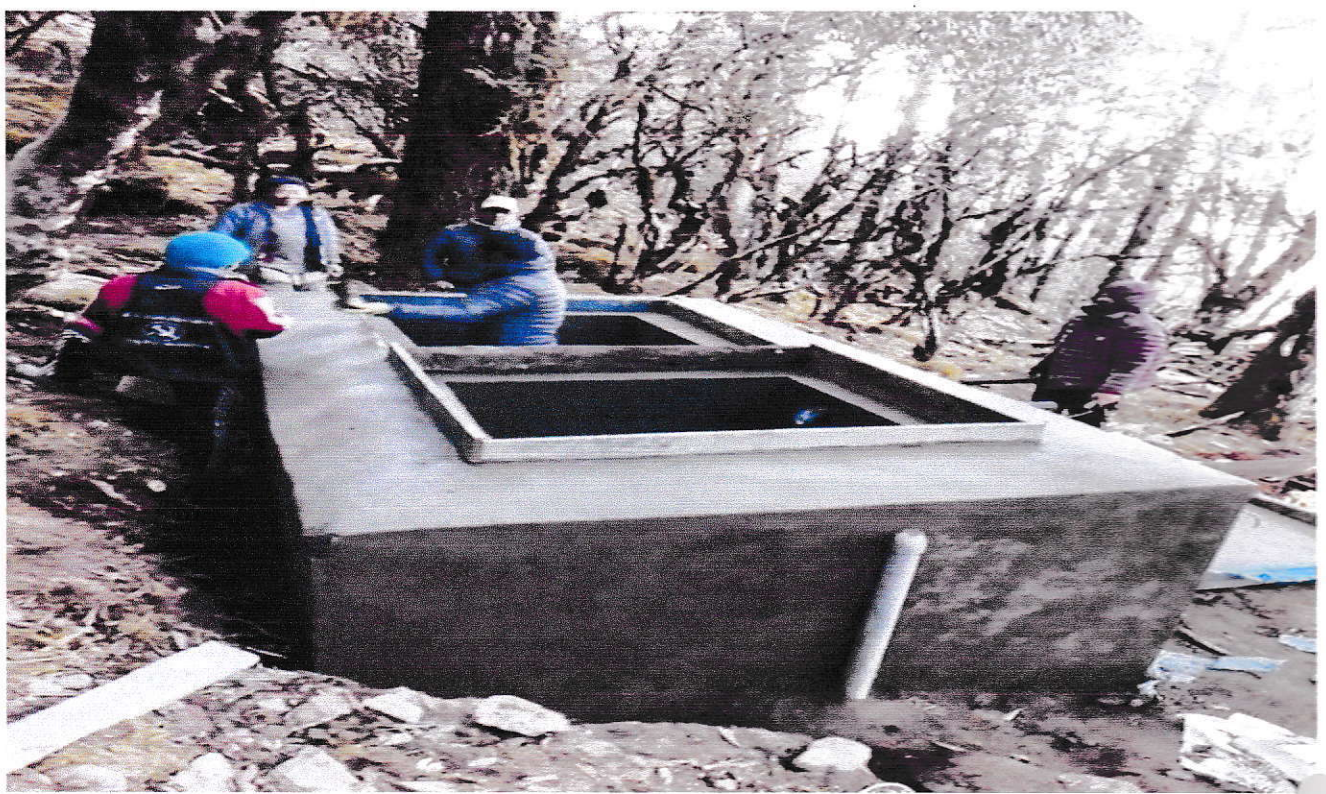

II Shree Ganeshaya: Namah: II



Bicky Hardware House Pvt. Ltd.

Sukedhara, Kathmandu

Ph No. : +977-1-4378352 / 4378353

Email : info@bickyhardwares.com

VAT No.:

6 0 0 6 2 9 3 2 4

TAX INVOICE

Branch : Sukedhara

Customer Details

CHANDESORI CONSTRUCTION

SOLUKHUBU

VAT No. : 605576856

Bill Details

Bill No. : SUK/05990

Bill Miti : 2079/01/25

Bill Date : 08/05/2022

Bill Type : Credit

Transaction Date : 08/05/2022

S.N.	PARTICULARS	QTY.	UNIT	RATE	AMOUNT
1.	GI PIPE 2.5". M	190.00	Pcs	6,946.91	1,319,912.90

Remarks : 9849042607

Vehicle No. : BA 2 KA 71

Driver : MAULA TAMANG

Mobile No. : 9869806249

In Words : Rs. One Million Four Hundred Ninety-One
Thousand Five Hundred One And Fifty-Eight
Paise Only

Basic Total : 1,319,912.90

Discount : 0.00

Labour Charges : 0.00

Freight Charges : 0.00

Taxable Amount : 1,319,912.90

Vat @13% : 171,588.68

Net Total : 1,491,501.58

* Goods once sold will not be taken back.

* E&OE

Print Date & Time :

Sunday, May 8, 2022

12:44:58 pm



NEPAL PLASTICS PVT. LTD..
DHARAN INDUSTRIAL ESTATE, DHARAN-8, TINKUNE

PAN NO:300016097

TAX INVOICE

3:31:04PM 01/06/2022

INVOICE TO M/S : CHANDESWARI CONSTRUCTION

Bill NO : SB-1808

Date : 01-Jun-2022

MITI : 18/02/2079

ADDRESS SOLUKHUMBU

Mode Of Payment :Credit

BUYER'S PAN NO.

6	0	5	5	7	6	8	5	6
---	---	---	---	---	---	---	---	---

 TEL NO.

S.No.	Particulars	Quantity	Unit	Rate	Amount
1	HDPE PIPE PE100 PN10*75MM	2,900.00	MTR	361.92	1,049,568.00
2	HDPE PIPE PE100 PN16*75MM	1,200.00	MTR	522.00	626,400.00
3	HDPE PIPE PE100 PN10*63MM	300.00	MTR	255.78	76,734.00
	HDPE PIPE PE100 PN10*32MM	400.00	MTR	67.86	27,144.00
	HDPE PIPE PE100 PN16*32MM	300.00	MTR	98.02	29,406.00
	HDPE PIPE PE100 PN12.5*25MM	50.00	MTR	50.17	2,508.50
In Words : Seventeen Lakh Sixty Thousand Six Hundred Sixty-Eight And Eighty-Five Paisa Only Remarks : AS PER SALES				Total	1,811,760.50
				Discount	-253,646.47
				Freight	0.00
				Taxable Amount	1,558,114.03
				VAT 13%	202,554.82
				Grand Total	1,760,668.85

Driver's Name :

Mobile No :

Vehicle No :

DHARAN INDUSTRIAL ESTATE, DHARAN-8, TINKUNE

TAX INVOICE

INVOICE TO M/S : CHANDESWARI CONSTRUCTION

Date : 15-Jun-2022

MITI : 01/03/2079

Mode Of Payment :Credit

Total	306,936.00
Discount	-42,971.04
Freight	0.00
Taxable Amount	263,964.96
VAT 13%	34,315.44
Grand Total	298,280.40

NEPAL PLASTIC PVT. LTD.

॥ Shree Ganeshaya: Namah: ॥



Bicky Hardware House Pvt. Ltd.

Sukedhara, Kathmandu

Ph No. : +977-1-4378352 / 4378353

Email : info@bickyhardwares.com

VAT No.:

6 0 0 6 2 9 3 2 4

TAX INVOICE

Branch : Sukedhara

Customer Details

CHANDESORI CONSTRUCTION

SOLUKHUMBU

VAT No. : 605576856

Bill Details

Bill No. : SUK/05993

Bill Miti : 2079/01/25

Bill Date : 08/05/2022

Bill Type : Credit

Transaction Date : 08/05/2022

S.N.	PARTICULARS	QTY.	UNIT	RATE	AMOUNT
1.	GI PIPE 2.5". M	110.00	Pcs	6,946.91	764,160.10
2.	GI FITTINGS -. SOCKET 2.5"	250.00	Pcs	309.74	77,435.00
3.	GI FITTINGS -. ELBOW 2.5"	50.00	Pcs	522.13	26,106.50

Remarks : 9849042607

Vehicle No. : KO 1 KH 7955

Driver : TANKA

Mobile No. : 9849815080

In Words : Rs.Nine Hundred Eighty Thousand Five
Hundred Two And Eighty-One Paise Only

Basic Total : 867,701.60

Discount : 0.00

Labour Charges : 0.00

Freight Charges : 0.00

Taxable Amount : 867,701.60

Vat @13% : 112,801.21

Net Total : 980,502.81

* Goods once sold will not be taken back.

* E&OE

Print Date & Time :

Sunday, May 8, 2022

1:37:10 pm

SUKEDHARA



VAT No. 603052796

"Commitment for Development"

TAX INVOICE

Firm Regd. No. 121001071072



MARUTI TRADINGS

Registered Government Suppliers

Sold to:

Chandeshwari Construction
Solukhumbi.

Invoice No. 252 Date: 5 May 2022

Challan No. _____ Date: _____

Order Ref. _____ PO

Terms: _____ Payment Against Delivery

VAT No.

6 0 5 5 7 6 8 5 6

Interest will be charged @ 18% p.a. if the payment is not made within 7 days from the date of the invoice

S. No.	Description	Size	Quantity	Rate	Amount	
					Rs.	Ps.
1	GI Strainer. 12" long	3"	1	972.00	972.00	
2	GI Reducer	3" x 2"	1	512.00	512.00	
	GI Pipe, M	2"	0.6	961.00	576.60	
	GI Union	2"	1	458.00	458.00	
	GI Nipple. 6" long	2"	1	201.00	201.00	
6	Brass Union	2"	1	1,173.00	1,173.00	
7	GI Pipe, M	3"	0.6	1,581.00	948.60	
8	GI End Cap	3"	1	190.00	190.00	
9	GI Socket	3"	1	440.00	440.00	
10	GI Elbow	2-1/2"	3	490.00	1,470.00	
11	GI Pipe, M	2-1/2"	135	1,214.00	1,638.90	
12	GI Nipple. 6" long	2-1/2"	1	759.00	259.00	
13	Flange Set	2-1/2"	3	1,350.00	4,050.00	
14	GI Strainer. 12" long	4"	1	1,454.00	1,454.00	
15	GI Reducer	4" x 2-1/2"	1	834.00	834.00	
16	GI Pipe, M	2-1/2"	0.6	1,214.00	728.40	
17	GI Pipe, M	1 1/2"	0.7	237.00	165.90	
18	GI Union	2-1/2"	1	854.00	854.00	
19	GI Nipple. 6" long	2-1/2"	3	259.00	777.00	
20	GI Unusual Tee	2-1/2" x 1/2"	1	710.00	710.00	
21	GI Foul Tee	1 1/2"	1	53.00	53.00	
22	Gate Valve	2-1/2"	1	7,840.00	7,840.00	
23	Flange Set	2"	1	1,170.00	1,170.00	
24	GI Pipe, M	3"	0.9	1,581.00	1,422.90	
25	GI Elbow	3"	1	660.00	660.00	
MARUTI TRADINGS				Sub Total	29,558.30	
				%Discount		
				Taxable Amount	29,558.30	
				...4.2...%VAT	3,842.58	
				Grand Total	33,400.88	
In words Rupees	Thousand	Hundred	Rupee		Paissa	
	Thirty Three	Four			Fifty Eight Only	

No claims accepted for breakage or shortage after delivery of goods.

Thanking you and Looking Forward
Goods Received In Good Condition

MARUTI

Goods once sold will not be taken back

E.&O.E

TRADINGS

For: MARUTI TRADINGS

Authorised Signatory

Signature of Buyer



MA 96

"Commitment for Development"

TAX INVOICE

Firm Regd. No. : 121001/071/072

old to : Chan

MARUTI TRADINGS

Registered Government Suppliers

Chandakwari Construction

Solukhumbu

VAT No.

6 0 5 5 7 6 8 5 6

Invoice No.

203

Date: 5 May 2022

Challan No.

Date:

Order Ref.

PO

Terms :

Payment Against Delivery

Interest will be charged @ 18% p.a. if the payment is not made within 7 days from the date of the invoice

S. No.	Description	Size	Quantity	Rate	Amount	
					Rs.	Ps.
1	GI Pipe, M	3"	0.9	1,581.00	1,422.90	
2	GI Union	3"	1	1,190.00	1,190.00	
3	GI Nipple, 6" long	3"	3	324.00	972.00	
4	Gate Valve *	3"	1	13,142.00	13,142.00	
	GI Equal Tee	3"	1	890.00	890.00	
6	GI / HDPE Flange Set	3"	1	2,025.00	2,025.00	
* कोरा - ४. * GI pipe - 3पस एके ठाउँ कोरको, काँडि pipe कोरामा हालेको छ।					Sub Total	
					19,641.90	
					%Discount	
					Taxable Amount	
					19,641.90	
					+.....%VAT	
					2,553.45	
					Grand Total	
					22,195.35	
Remarks				7.9		
					In words	
					Thousand	
					Hundred	
					Rupee	
					Paise	
					Twenty Two	
					One	
					Ninety Five	
					Thirty Five Only	

No claims accepted for breakage or shortage after delivery of goods.

Thanking you and Looking Forward

Goods Received in Good Condition

MARUTI

Goods once sold will not be taken back

E.&O.E

MARUTI

For: MARUTI TRADINGS

Authorised Signatory

Signature of Buyer

Milan Marg, Kathmandu, Ph.: 01-4242045, Email : tradingsmaruti@gmail.com

VAT No. 603052796

"Commitment for Development"

TAX INVOICE

Firm Regd. No. : 121001/071/072

MARUTI



TRADINGS

MARUTI TRADINGS

Registered Government Suppliers

Sold to: Chandeshwor Construction
Solukhumbu

Invoice No. 275 Date: 2079/2/26

Challan No. — Date: —

Order Ref. Verba)

Terms: Against Delivery.

VAT No. 605576856

Interest will be charged @ 18% p.a. if the payment is not made within 7 days from the date of the invoice

S. No.	Description	Size	Quantity	Rate	Amount	
					Rs.	Ps.
①	Main hole Cover, Circular 24"	600 mm	12 pcs.	1895/-	22,740/-	
Remarks					Sub Total 22,740/-	
					%Discount —	
					Taxable Amount 22,740/-	
					%VAT 2956/20	
					Grand Total 25,696/20	
In words Rupees	Thousand	Hundred	Rupee		Paissa	
	Twenty five	Six	Ninety six		Twenty only	

No claims accepted for breakage or shortage after delivery of goods.

Thanking you and Looking Forward

Goods Received in Good Condition

Signature of Buyer

MARUTI

Goods once sold will not be taken back

E.&O.E



TRADINGS

For: MARUTI TRADINGS

Authorised Signatory

Milan Marg, Kathmandu. Ph.: 01-4242045. Email: tradingsmaruti@gmail.com



Shubha Shree Jagdamba Cement Mills Pvt. Ltd.

Corporate Office: Neupane Tower, 6th Floor, Tinkune, Kathmandu, Nepal
Tel.: 01-4111500/ 550/ 633, Fax No.: 01-4111634, Facebook: jagdamba.cement

Factory Office: Birgunj-32, Chorni, Parsa, Nepal, Tel.: 051-419903/05

PAN No.: 3 0 2 6 3 8 6 3 3

Website: www.jagdambacement.com

TAX-INVOICE

Consignee Name & Detail :

Customer Name: CHANDESHWORI CONSTRUCTION

Address : SOLU,,

PAN NO : 605576856

Invoice No. : SB/23013
Invoice Date : 28/05/2022 14/02/2079
Order No. :
Order Date : 28/05/2022 14/02/2079
Vehicle No : NA6KH8327
Destination : SOLU
Contact No. :

Mode Of Payment Through Account Payee Cheque or Swift Only.

S.N.	Description of Goods	Unit	Qty.	Rate/Unit	Amount
1	OPC ULTRA PREMIUM (43 GRADE)	BAG	339.000	572.450	194,060.55
Total			339.00	Sub Total	194,060.55
			Excise Duty@Rs	11.00	3,729.00
			Discount Rs	33 per Bag	-11,187.00
			Taxable Amount		186,602.55
			13 % VAT		24,258.33
			Grand Total		210,860.88

Amount In Words: NRS Amount Chargeable (in Words) :Two Lakh Ten Thousand Eight Hundred Sixty And Eighty-Eight Paise Only

E.& O.E Remarks :

Declaration : We declare that this invoice shows the actual price of the goods described and that all particulars are true and correct.

NAIM 14 Created By	Received the Material in Good Condition Receiver's Signature and Seal By	For :Shubha Shree Jagdamba Cement Mills Pvt. Ltd. 14 Authorised Signatory
--------------------------	---	---
